


RAED NARRATIVE REPORT FOR CY 2013

For 2013, the Regional Agricultural Engineering Division (RAED) continues to render major technical support for the effective, efficient and successful implementation of various Pre-Harvest Farm Machineries, Post-Harvest Facilities, Irrigation, Farm-to-Market Roads and other Agri-Related Infrastructure Projects and to include other Big Ticket Projects of the different Agri-Pinoy Programs and Special Projects in the region. It contributes to the validation, identification of sites monitoring and evaluation of projects in coordination with the different APP Coordinators and Project Leaders.

Further, technical personnel also contribute in the pro-active preparation of Specifications, Detailed Engineering Designs (DED) and Program of Works (POW) and other pertinent documents prior to bidding procedures.

For Farm-to-Market Road projects, the region had a total allocation of Php123,362,992.00 based on Special Allotment Release Order (SARO) released to complete the 37.10 kilometers road length under the Regular Funds. Some of these projects were already 100% accomplished while others are still on progress. Six (6) FMR projects were implemented by the department through public bidding, two (2) projects implemented by DPWH-District Engineering Offices, 15 projects by the local government units (LGUs) through a Memorandum of Agreement (MOA).

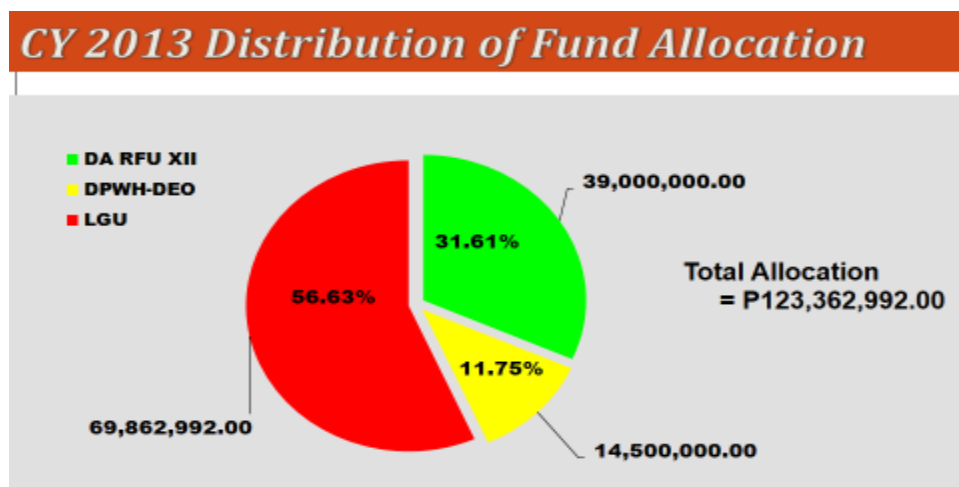

PROVINCE	No. of Projects	Allocation / Project Cost	Target Length (km)	Relative Weight (%)	% Accomplishment	Remarks
DA Implemented Projects	6	39,000,000.00	6.60	31.61%	15.76%	
Cotabato Province	5	29,000,000.00	5.48	23.51%	15.76%	2 projects completed / 3 on progress
South Cotabato Province	1	10,000,000.00	1.12	8.11%	0.00%	Awarded on December 27, 2013
DPWH-DEO Implemented Projects	2	14,500,000.00	2.00	11.75%	3.28%	
South Cotabato Province	2	14,500,000.00	2.00	11.75%	3.28%	1 project on progress / 1 for bidding
LGU Implemented Projects	15	69,862,992.00	28.50	56.63%	9.17%	
Cotabato Province	8	35,362,992.00	15.00	28.67%	5.12%	3 projects on progress / 5 for bidding
South Cotabato Province	7	34,500,000.00	13.50	27.97%	4.05%	6 projects on progress / 1 for bidding
TOTAL	23.00	123,362,992.00	37.10	100%	28.22%	

RAED also facilitated the implementation of FMR projects under the Bottom-Up Budgeting (BUB) Regular amounting to Php105,526,874.00, BUB-Special

Purpose Fund amounting to Php13,600,000.00 and P~~A~~Yapa at M~~A~~Saganang Pamaya~~N~~A~~N~~ (PAMANA) programs of about Php21,000,000.00.

Province / District	Name of Project / Location	Project Cost	Implementing Agency	Obligated	Status/Remarks
BUB FUND					
Cotabato		47,419,074.00		47,219,074.00	
District I		22,800,000.00		22,800,000.00	
	Rehabilitation of Calija-Beltran Road, Pisan, Kabacan	4,100,000.00	MLGU	4,100,000.00	20% on progress
	Rehabilitation of Malengen-Little Baguio FMR, Libungan	5,000,000.00	MLGU	5,000,000.00	on progress
	Rehabilitation of Poblacion-Gumaga FMR, Libungan	5,100,000.00	MLGU	5,100,000.00	on progress
	Construction/ Rehabilitation of Nunguan-Balungis FMR, Pikit	8,600,000.00	MLGU	8,600,000.00	70% on progress
District II		24,619,074.00		24,419,074.00	
	DA (Road Spot Concreting Brgy. Kamada Proper - Sitio River Side FMR, Magpet	2,969,074.00	MLGU	2,969,074.00	20% on progress
	Costruction of Meocan-Katindu- Mahongcog FMR, Arakan	2,450,000.00	MLGU	2,450,000.00	1st tranche released October 2013
	Rehabilitation of Imelda-Tamped-Taguranao FMR, Matalam	7,400,000.00	MLGU	7,400,000.00	80% on progress
	Rehabilitation of Datu Inda Guinto FMR, Pres. Roxas	5,800,000.00	MLGU	5,800,000.00	45% on progress
	Rehabilitation of Sitio Tarinan-Salat FMR, Pres. Roxas	6,000,000.00	MLGU	5,800,000.00	45% on progress
Sultan Kudarat		37,357,800.00		36,179,867.68	
District I		9,974,000.00		9,806,964.13	
	Rehabilitation of Tabunda/Almarza FMR, Tinumiguez, Lambayong	4,000,000.00	MLGU	4,000,000.00	42% on progress
	Rehab of Manili - Sampao Road, Lutayan	3,800,000.00	DA RFU XII	3,632,964.13	for implementation
	Rehabilitation of Poblacion-Bannawag FMR, Pres. Quirino	2,174,000.00	MLGU	2,174,000.00	for implementation
District II		27,383,800.00		26,372,903.55	
	Rehabilitation of Pamantingan to Marguez FMR, Esperanza	5,800,000.00	MLGU	5,800,000.00	1st tranche released
	Rehab of Ponpongan Malayat FMR, Kalamansig	6,000,000.00	MLGU	6,000,000.00	on progress
	Repair/Rehab and Construction of Barurao-Kinudalan Road, Lebak	6,434,000.00	MLGU	6,434,000.00	for 1st tranche
	Construction of Circumferential FMR in Badiangon, Palimbang	7,000,000.00	DA RFU XII	5,989,103.55	42.68% on progress
	Repair/Rehab and Construction of Hwy. Jct. - Kadi-Sepali FMR, SNA	2,149,800.00	MLGU	2,149,800.00	for 1st tranche
Sarangani		10,750,000.00		10,750,000.00	
Lone District		10,750,000.00		10,750,000.00	
	Improvement of Laguimit-Gulo FMR, Glan	1,500,000.00	MLGU	1,500,000.00	on progress
	Rehabilitation of Daan Suyan FMR (near base of the hanging Bridge), Malapatan	50,000.00	MLGU	50,000.00	1st Tranche released
	Construction of Panamin FMR (Brgy. Proper), Malungon	2,000,000.00	MLGU	2,000,000.00	for 1st tranche
	Construction of FMR - Box Culvert, Malungon	1,500,000.00	MLGU	1,500,000.00	for 1st tranche
	Construction of Columbio FMR (Sitio Balite), Brgy. San Roque	2,000,000.00	MLGU	2,000,000.00	for 1st tranche
	Construction of 60LM by 1.2 LM Span Cable Footbridge, Bagong Silang to Sitio Malalag Tubig, Brgy. Ampon	300,000.00	MLGU	300,000.00	for 1st tranche
	Construction of 20LM by 1 LM Span Cable Footbridge, Sitio Sto. Niño to Sitio Taclobo, Upper Mainit	300,000.00	MLGU	300,000.00	for 1st tranche
	Construction of B'laan FMR (Brgy. Proper to Datal Bago)	3,100,000.00	MLGU	3,100,000.00	for 1st tranche
Cotabato City		10,000,000.00		9,973,018.30	
	Concreting of Poblacion I FMR	10,000,000.00	DA RFU XII	9,973,018.30	40.5% on progress
TOTAL		105,526,874.00		104,121,959.98	
Special Purpose Fund (SPF)					
Cotabato		8,600,000.00		8,600,000.00	
District I		7,600,000.00		7,600,000.00	
	3 Rehabilitation of Liliongan - Sitio Abante, Sitio Spring - Liliongan Peripheral Road, Carmen	5,500,000.00	MLGU	5,500,000.00	50% on progress
	1 Opening/Construction of 0.80km FMR to designated production Areas, Pigcawayan	2,100,000.00	MLGU	2,100,000.00	20% on progress
District II		1,000,000.00		1,000,000.00	
	2 Rehabilitation of Kisupaan - Sitio Kabinuangan FMR, Pres.	1,000,000.00	MLGU	1,000,000.00	75% on progress
Sultan Kudarat		2,000,000.00		2,000,000.00	
District II		2,000,000.00		2,000,000.00	
	Rehabilitation of Panamin Campo to Sumilin, Bagumbayan	2,000,000.00	MLGU	2,000,000.00	on progress
Sarangani		3,000,000.00		3,000,000.00	
Lone District		3,000,000.00		3,000,000.00	
	Sitio Molo - Sitio Lambating FMR, Malapatan	1,500,000.00	MLGU	1,500,000.00	1st Tranche released
	Sitio Proper - Sitio Sulkili, Malapatan	1,500,000.00	MLGU	1,500,000.00	1st Tranche released
Cotabato City					
TOTAL		13,600,000.00		13,600,000.00	
PAMANA FUND					
Cotabato		21,000,000.00		21,000,000.00	
District II		21,000,000.00		21,000,000.00	
	2 Construction/Rehabilitation of Kabalantian - Lower Lumbo / Benaton / Kapayahan / Bagong Silang Farm to Market Road, Arakan	21,000,000.00	MLGU	21,000,000.00	1st Tranche December 2013
TOTAL		21,000,000.00		21,000,000.00	
